Project Planning Phase
Project Planning Template

Date	08 March 2026
Team ID	MCA_DA2
Project Name	Plugging into the Future: An Exploration of Electricity Consumption Patterns
Maximum Marks	8 Marks

Product Backlog & Sprint Schedule

Sprint	Epic	Story No.	User Story / Task	Points	Priority	Member
Sprint-1	Data Collection	USN-1	As a data engineer, I can load Consumption.csv into MySQL and verify 16,600 rows are loaded correctly.	3	High	Divyansh
Sprint-1	Data Validation	USN-2	As an analyst, I can run Python validation to confirm 0 nulls, 33 states, correct date range.	2	High	Faisal
Sprint-2	Tableau Setup	USN-3	As a BI dev, I can connect Tableau to MySQL and create 5 calculated fields: Month, Year, Quarter, Phase, YoY%.	3	High	Faisal
Sprint-2	Visualisations	USN-4	As a user, I can view 2019 and 2020 State Consumption bar charts for all 33 states.	2	High	Kali / Ishita
Sprint-3	Visualisations	USN-5	As a user, I can view Total Consumption, Usage by Region, and Top N/Bottom N charts.	3	High	Kali / Ishita
Sprint-3	Visualisations	USN-6	As a user, I can see a dual-axis 2019 vs 2020 monthly line chart showing the June 2020 collapse.	3	High	Faisal
Sprint-4	Visualisations	USN-7	As a user, I can view Before/After Lockdown bar, Region stacked bar, Quarter, and Metro City charts.	4	High	Faisal

Sprint-5	Dashboard	USN-8	As a user, I can interact with 3 dashboards (Overview, Lockdown, Recovery) with all filters working.	5	High	Faisal
Sprint-5	Story	USN-9	As a user, I can navigate a 5-scene Tableau Story with trend, regional, lockdown, rankings, recovery.	3	High	Faisal
Sprint-6	Publishing	USN-10	As a developer, I can publish to Tableau Public and embed in Flask web app at /dashboard and /story.	3	High	Divyansh
Sprint-6	Documentation	USN-11	As a team, I record a 5–7 min video explaining the project end-to-end and complete all documents.	2	High	Faisal

Sprint Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Story Points	Duration	Start Date	End Date (Planned)	Points Done	Actual Release
Sprint-1	5	1 Day	Feb 26, 2026	Feb 27, 2026	5	Feb 27, 2026
Sprint-2	5	1 Day	Feb 27, 2026	Feb 28, 2026	5	Feb 28, 2026
Sprint-3	6	1 Day	Feb 28, 2026	Feb 28, 2026	—	—
Sprint-4	4	2 Days	Feb 28, 2026	March 2, 2026	—	—
Sprint-5	8	2 Days	March 2, 2026	March 4, 2026	—	—
Sprint-6	5	5 Days	March 4, 2026	Mar 9, 2025	—	—
TOTAL	33	12 Days	Feb 26, 2026	Mar 9, 2025	10 (S1+S2)	—

Velocity: AV = Total Points / Sprints Completed = (5+5) / 2 = 5 points per sprint

Remaining points: 33 - 10 = 23 | Sprints needed: 23 / 5 = ~4.6 → ON TRACK to finish by Mar 09, 2025

Burndown Chart Note:

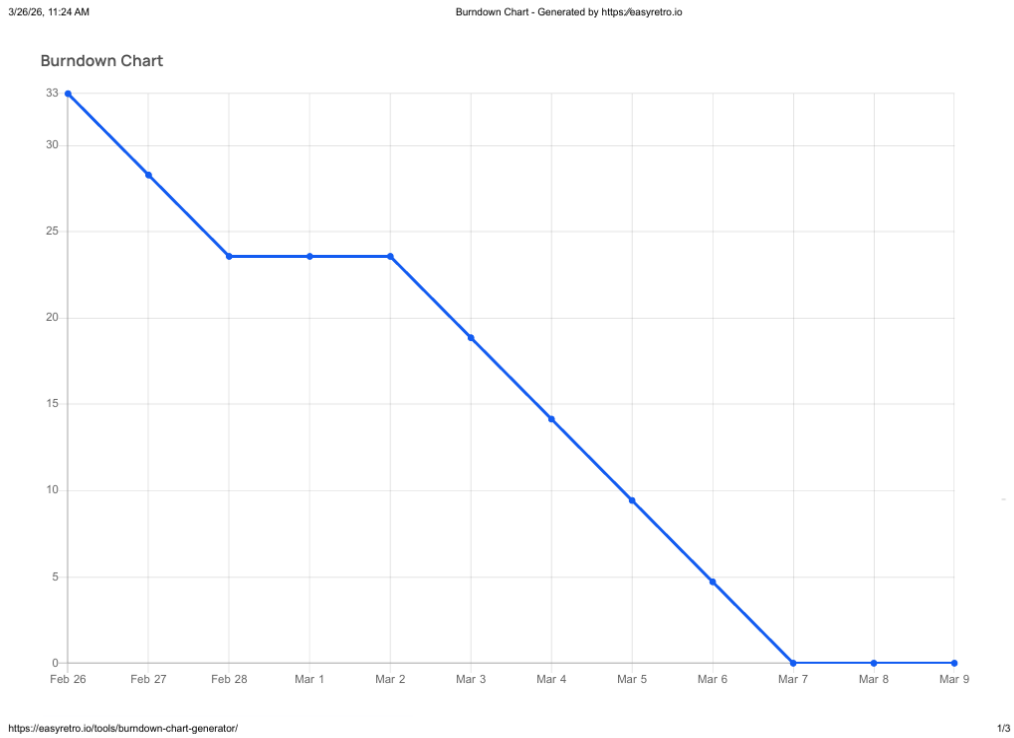

X-axis: Time spent (in days) | Y-axis: Story points remaining | Plot two lines: Ideal (33→0) and Actual (updated each sprint).
